



ABU DHABI CYCLE TRACK PROJECT



Progress Status
Dec 2025



Projects Highlight



	TRACK 01		TRACK 02		TRACK 03 & 04	HSCT
	Package 1 & 2	Package 3 & 4	Part 1	Part 2		
Distance (Planned)	105km	69.1km	37 km	25km	126km	52 km
Current Stage	Construction	Construction	Design & Build Construction	Design & Build Construction	Design & Build Construction	Design
Construction Contract Cost*	168m	185m	445m	Base: 130Mn Overall : 889Mn	328m	TBC
Contractor	Gulf Contracting & Landscape	Hilalco	Western Bainoona Group	Western Bainoona Group	GCC Landscape	TBD-Under Design

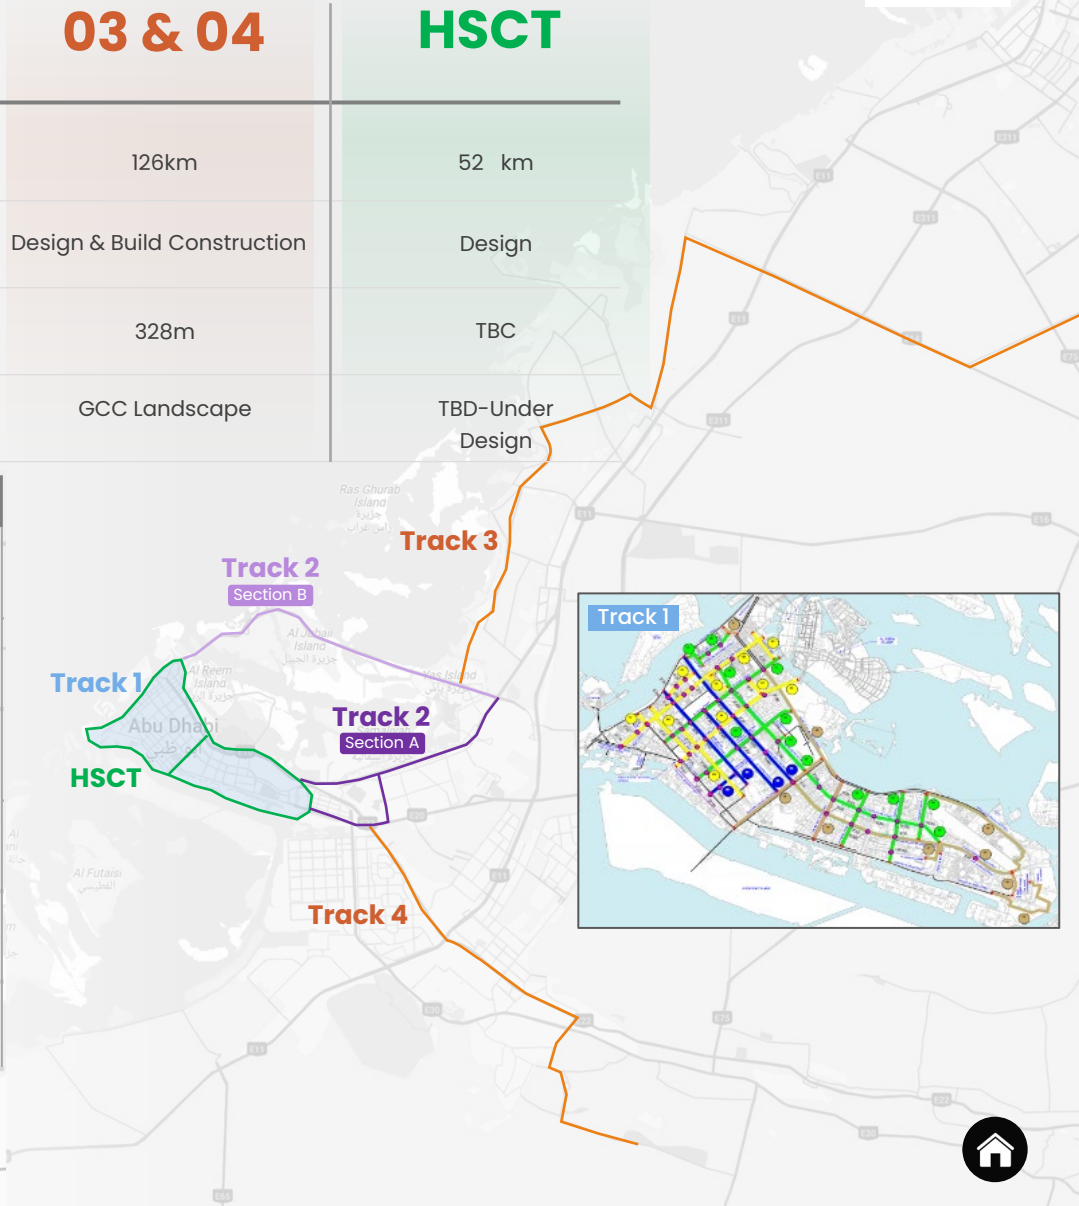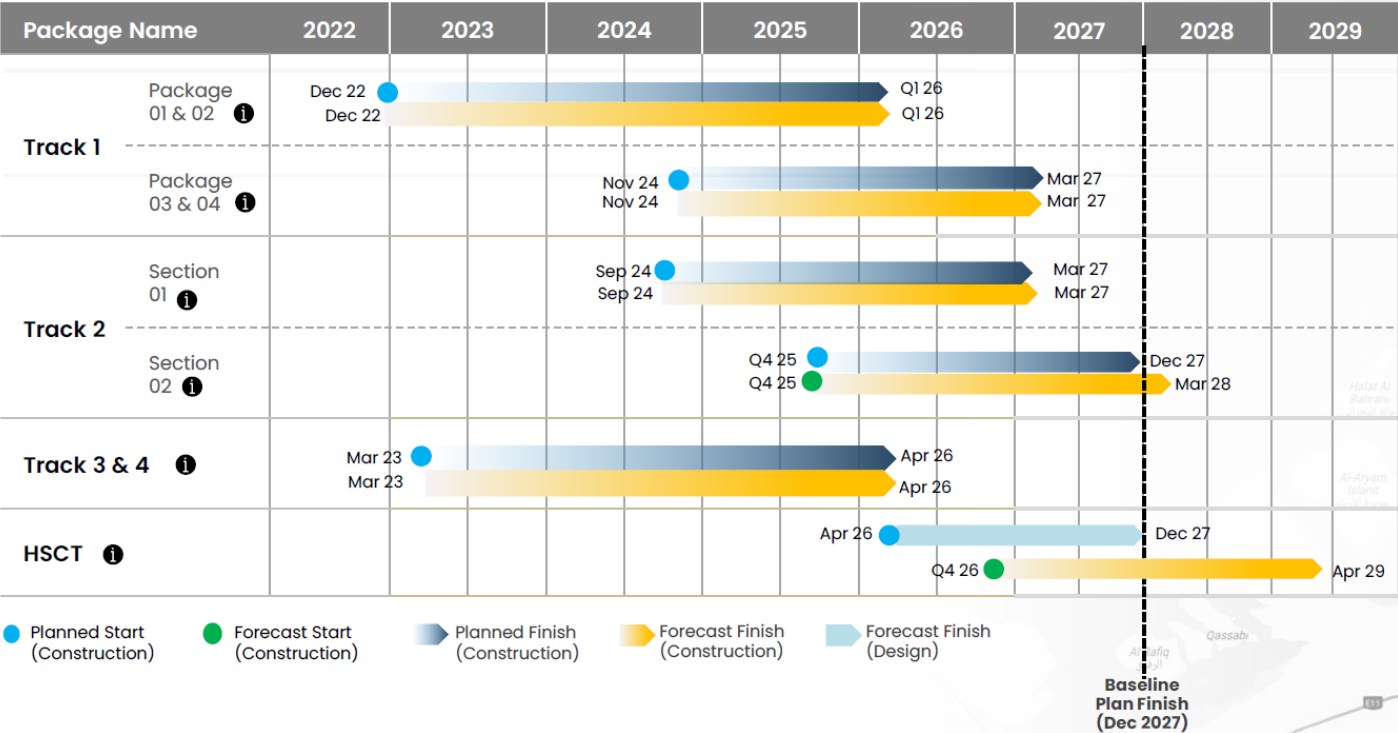


TRACK 01
(PACKAGE 01 & 02)

New Cycle Track
105.7 km

PROJECT LAYOUT

Package 1 - 9 Streets / 48.3 Km

Package 2 - 10 Streets / 57.4 Km

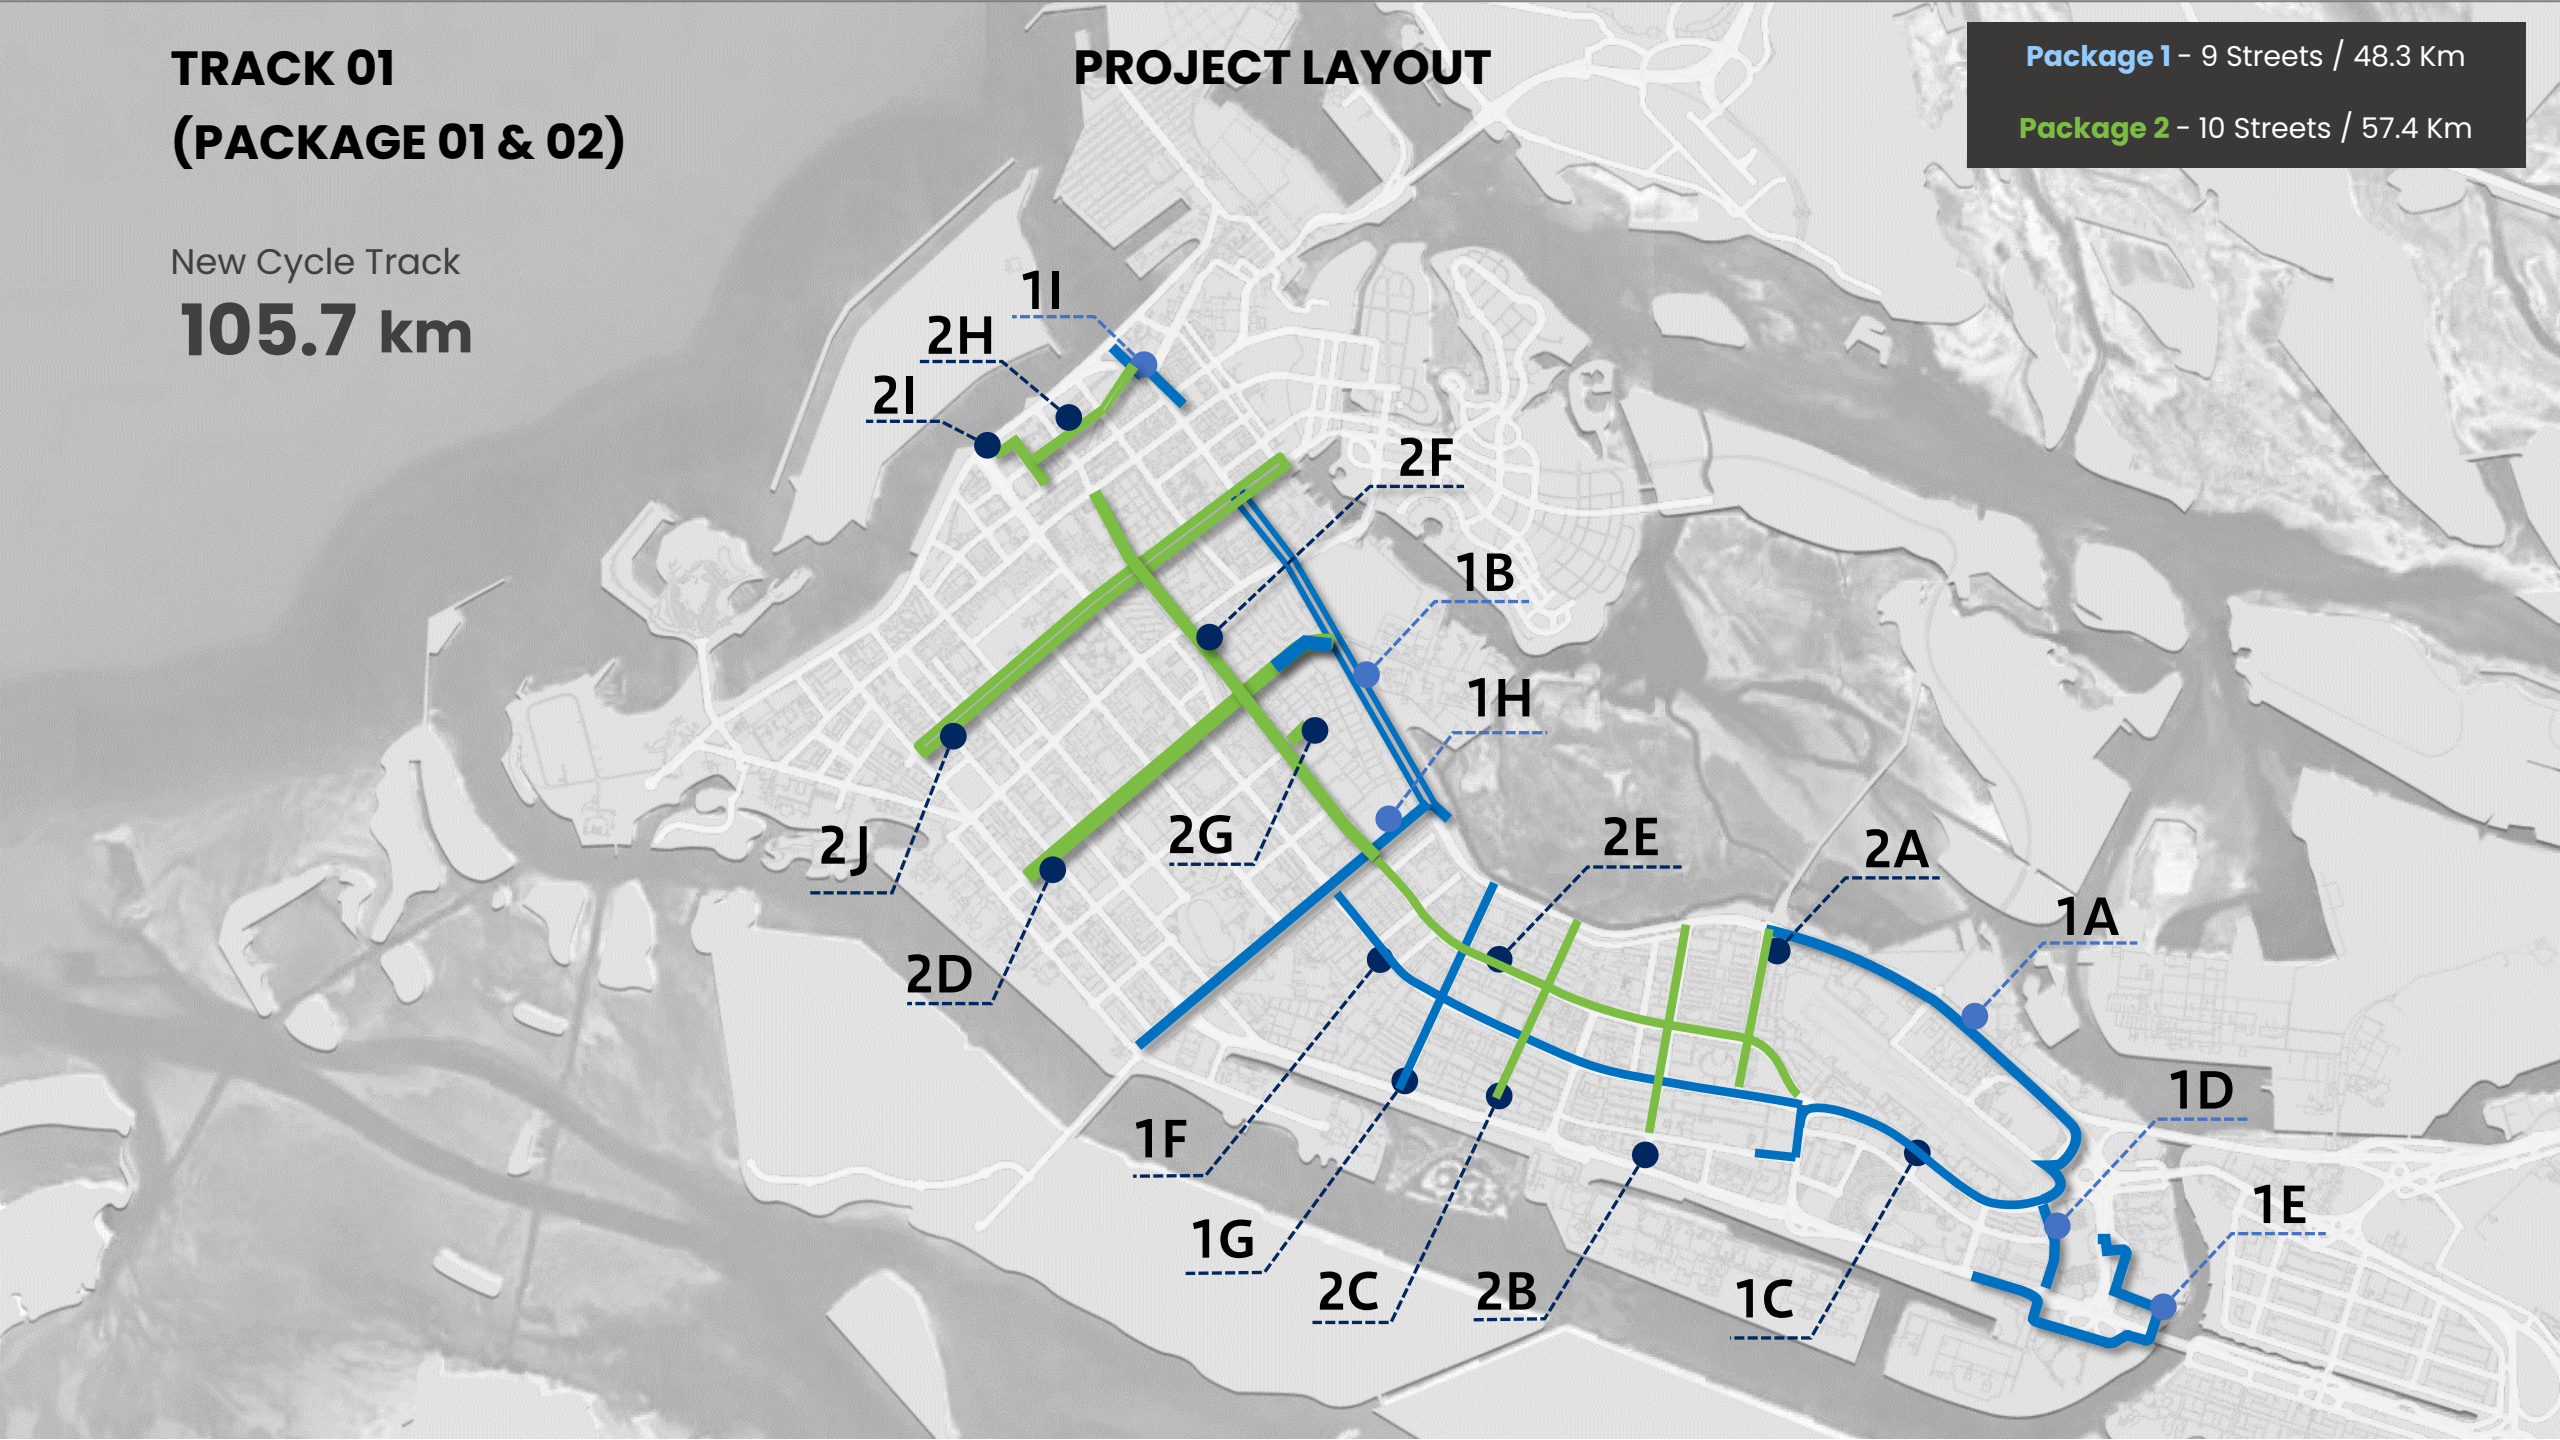

TRACK 01, PACKAGE 01 & 02 PROGRESS LAYOUT



Date: 20 Dec. 2025
Scope: 105.7 km
Completed: 86.7 km

- Completed track
- Existing track
- Work in Progress
- De-scoped / scope transfer
- Re-design track

TRACK 01

(Package 01 & 02)



Design Status

Completed



Contractor Procurement

Completed



Construction

Ongoing

FEB 2026

Forecast Completion




Description

The project aims to build 105.7 km of cycle tracks across 19 streets in Abu Dhabi Island to support the increasing number of cyclists using bikes and scooters for commuting, recreation, and sports.

Key KPIs

Cycle track length	105.7 km
No. of Streets	19
Forecasted ccompletion	Feb 2026



86.7 km asphalt work has been completed out of 105 km



Subgrade Work
3B (Segment 3 - Right Side)



Asphalt Work
2G (Segment 1 - Left Side)



Subbase Work
2B (Segment 1 - Left Side)




TRACK 01 (PACKAGE 03 & 42)

New Cycle
Track
69.1 km
14 Streets

PROJECT LAYOUT

Base Scope - 43.17 km / 9 Streets

Optional Scope - 25.93 km / 5 Streets

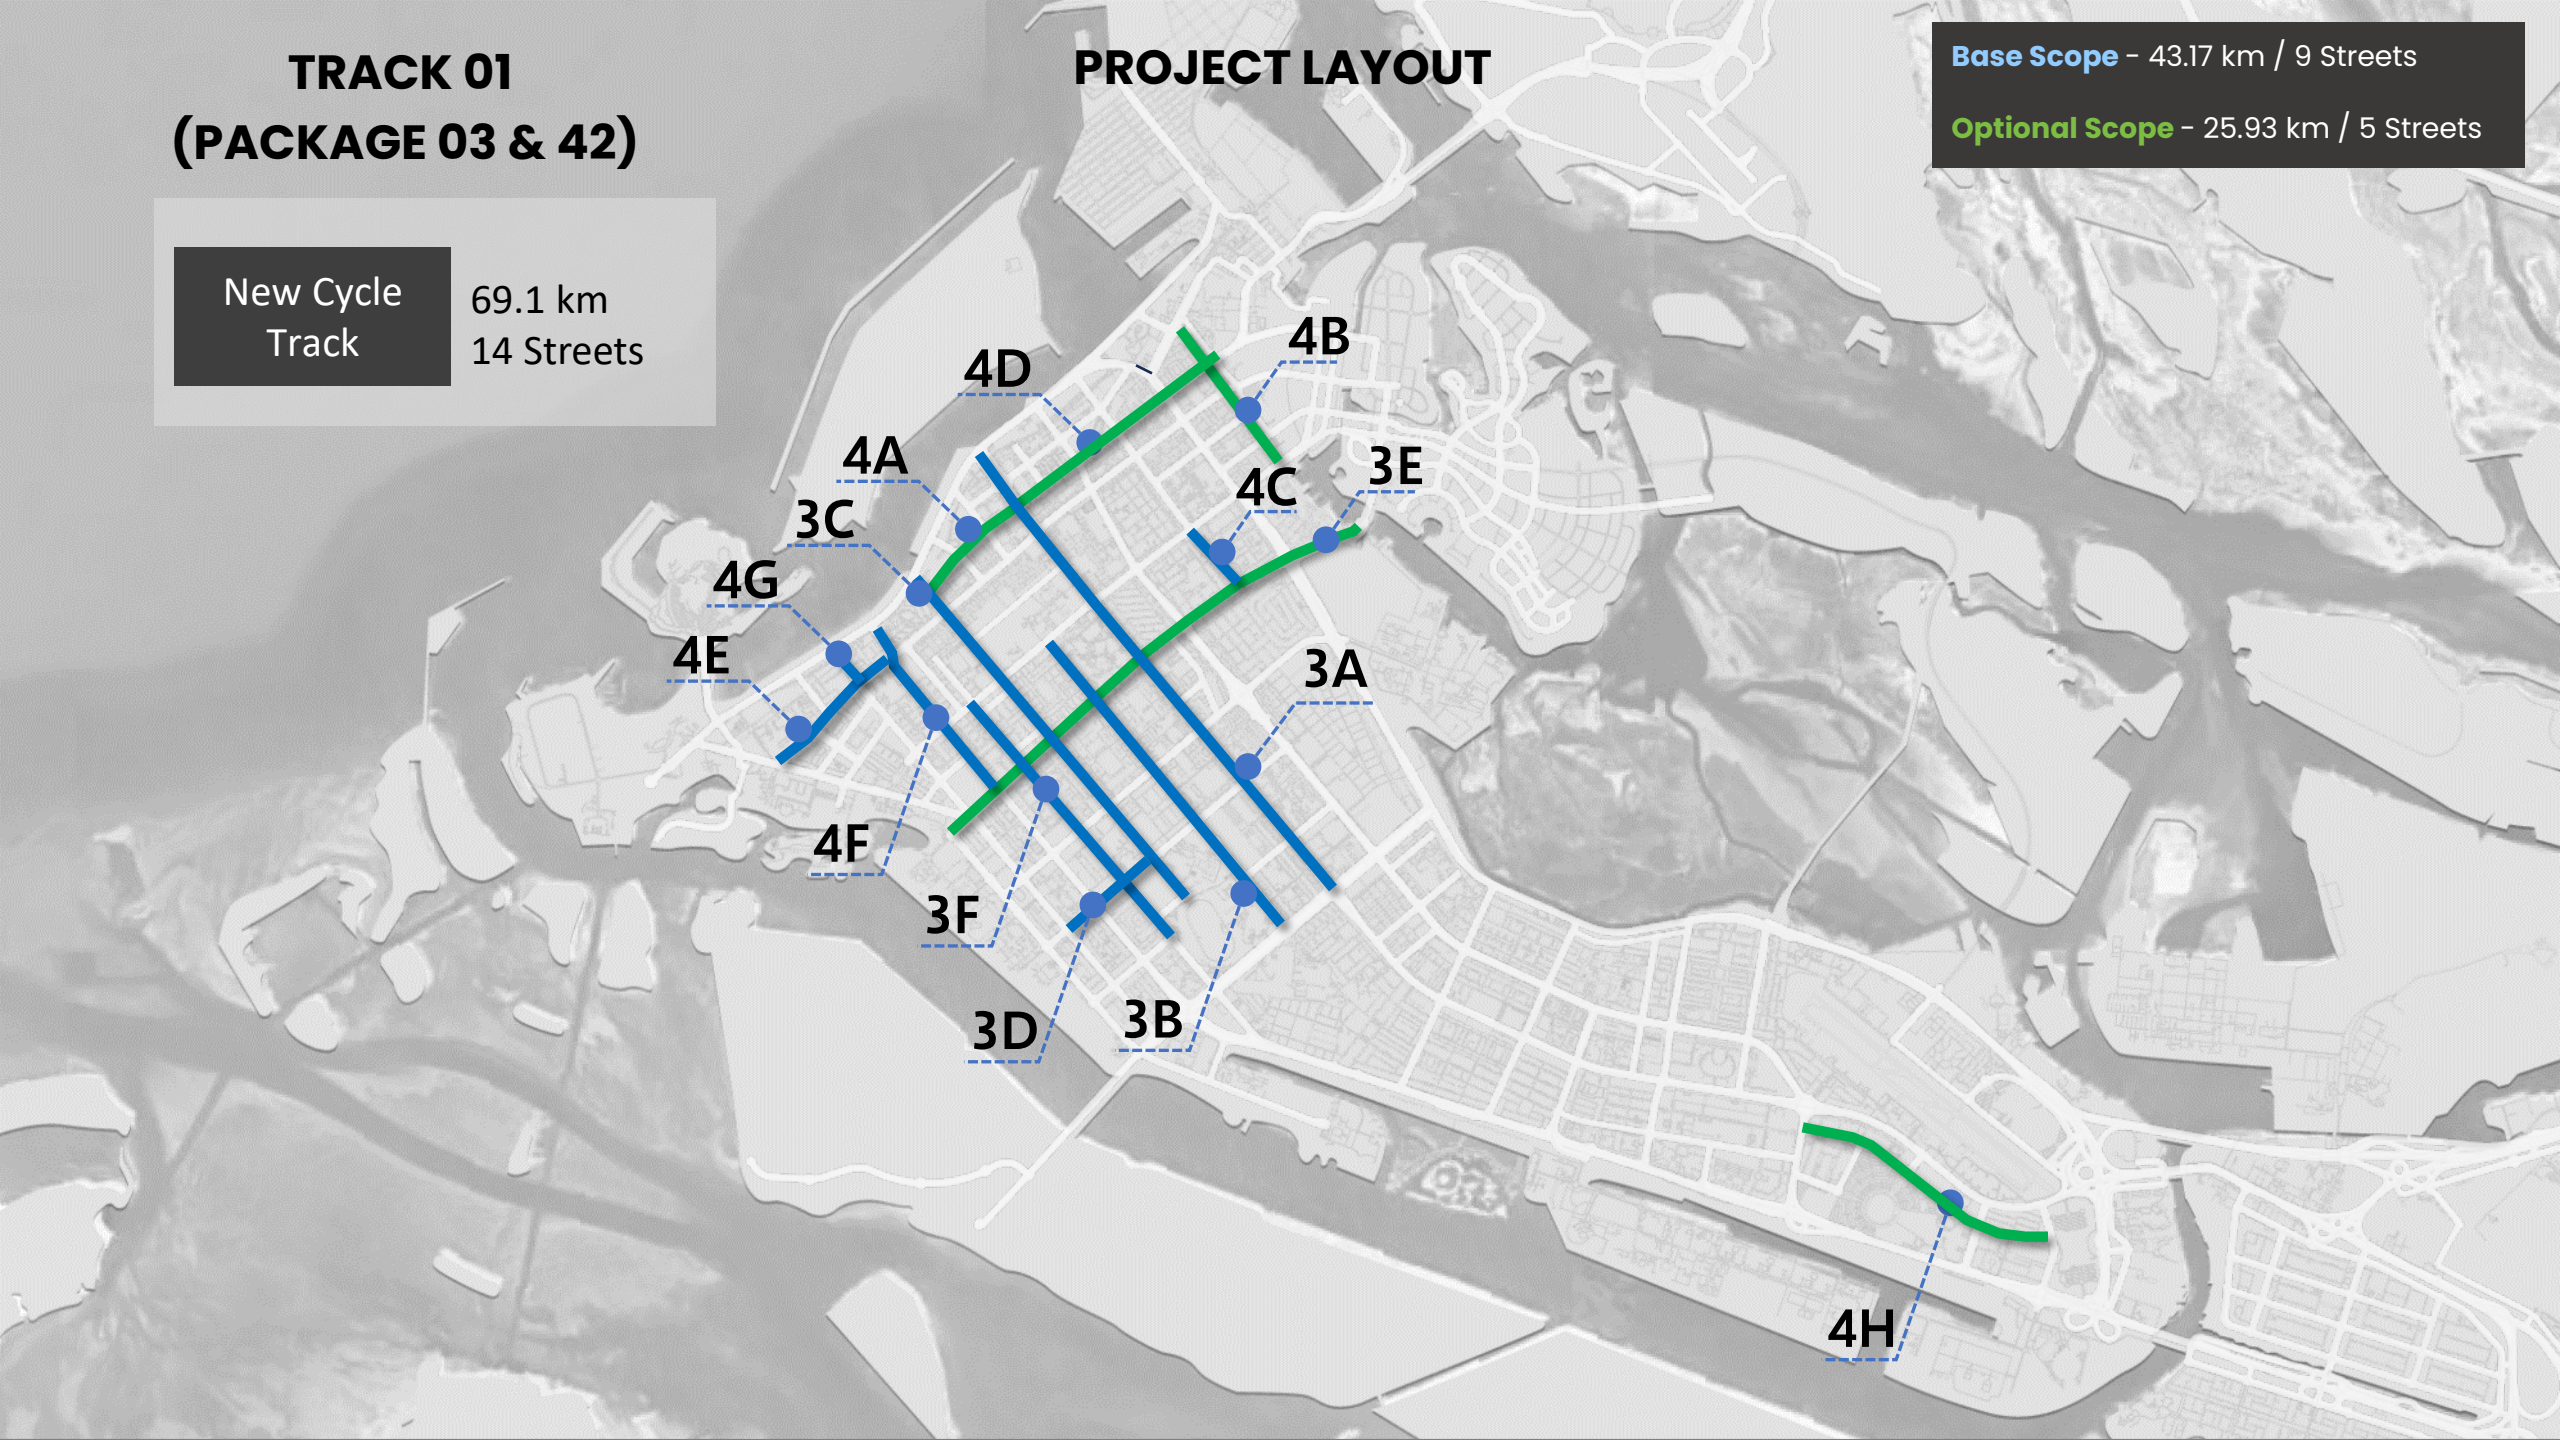

TRACK 01, PACKAGE 03 & 04 PROGRESS LAYOUT



3A

3B

4F

3C

3F

Date: 20 Dec. 2025
Scope: 69.1 km
Completed: 10.3 km

- Work in Progress
- Asphalt Completed
- Existing Track

TRACK 01

(Package 03 & 04)



Design Status

Completed



Contractor Procurement

Completed



Construction

Ongoing

MAR 2027

Forecast Completion



Description

The project aims to build 69.1 km of cycle tracks across 14 streets on Abu Dhabi Island to support the increasing number of cyclists using bikes and scooters for commuting, leisure, and sports.

Key KPIs

Cycle track length	69.1 km
No. of Streets	14
Forecasted completion	March 2027



10.3 km asphalt work has been completed out of 69 km



Excavation & Formation
4F (Segment 1 - Right



Subgrade Work
2D (Segment 1 - Right Side)



Subbase Work
2I (Segment 1)



TRACK 03 & 04


Track – Progress Layout


Design Status
Completed


Contractor Procurement
Completed D&B


Construction
Ongoing

APR 2026
Forecast
Completion

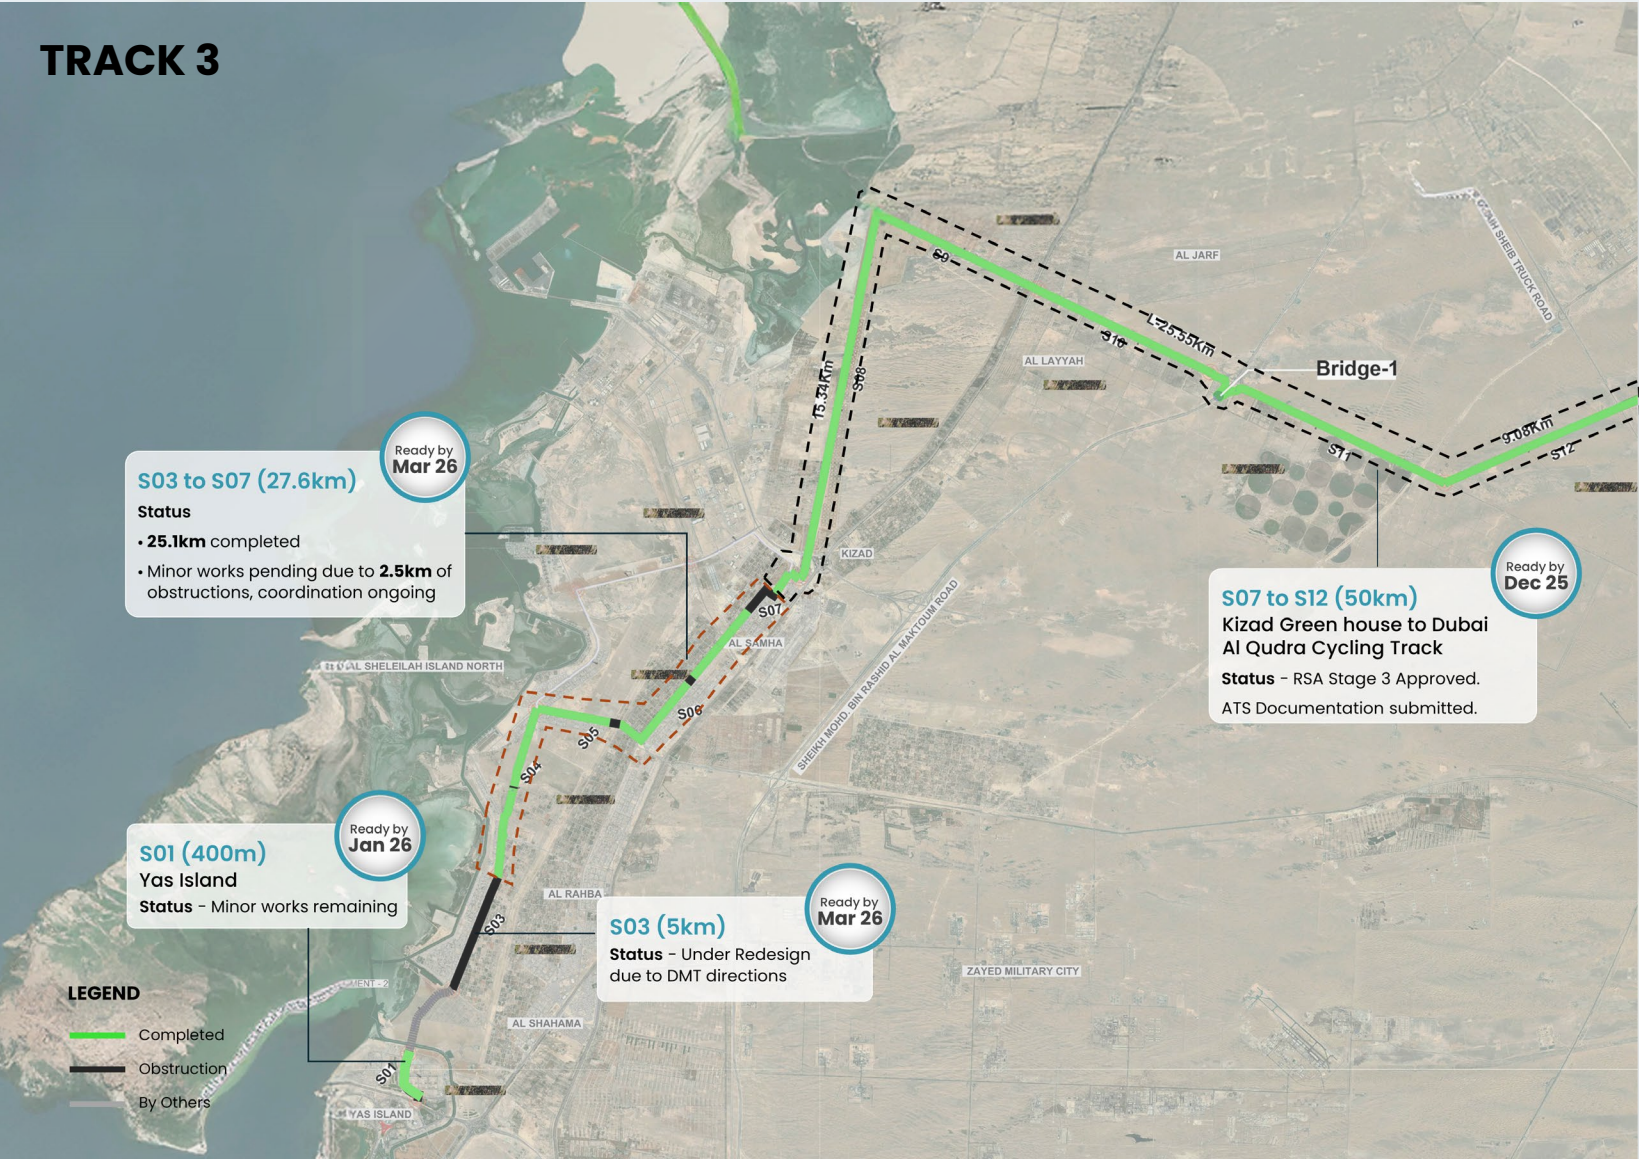

TRACK 03 & 04


Track 4 – Progress Layout


Design Status
Completed


Contractor Procurement
Completed D&B


Construction
Ongoing

APR 2026
Forecast
Completion

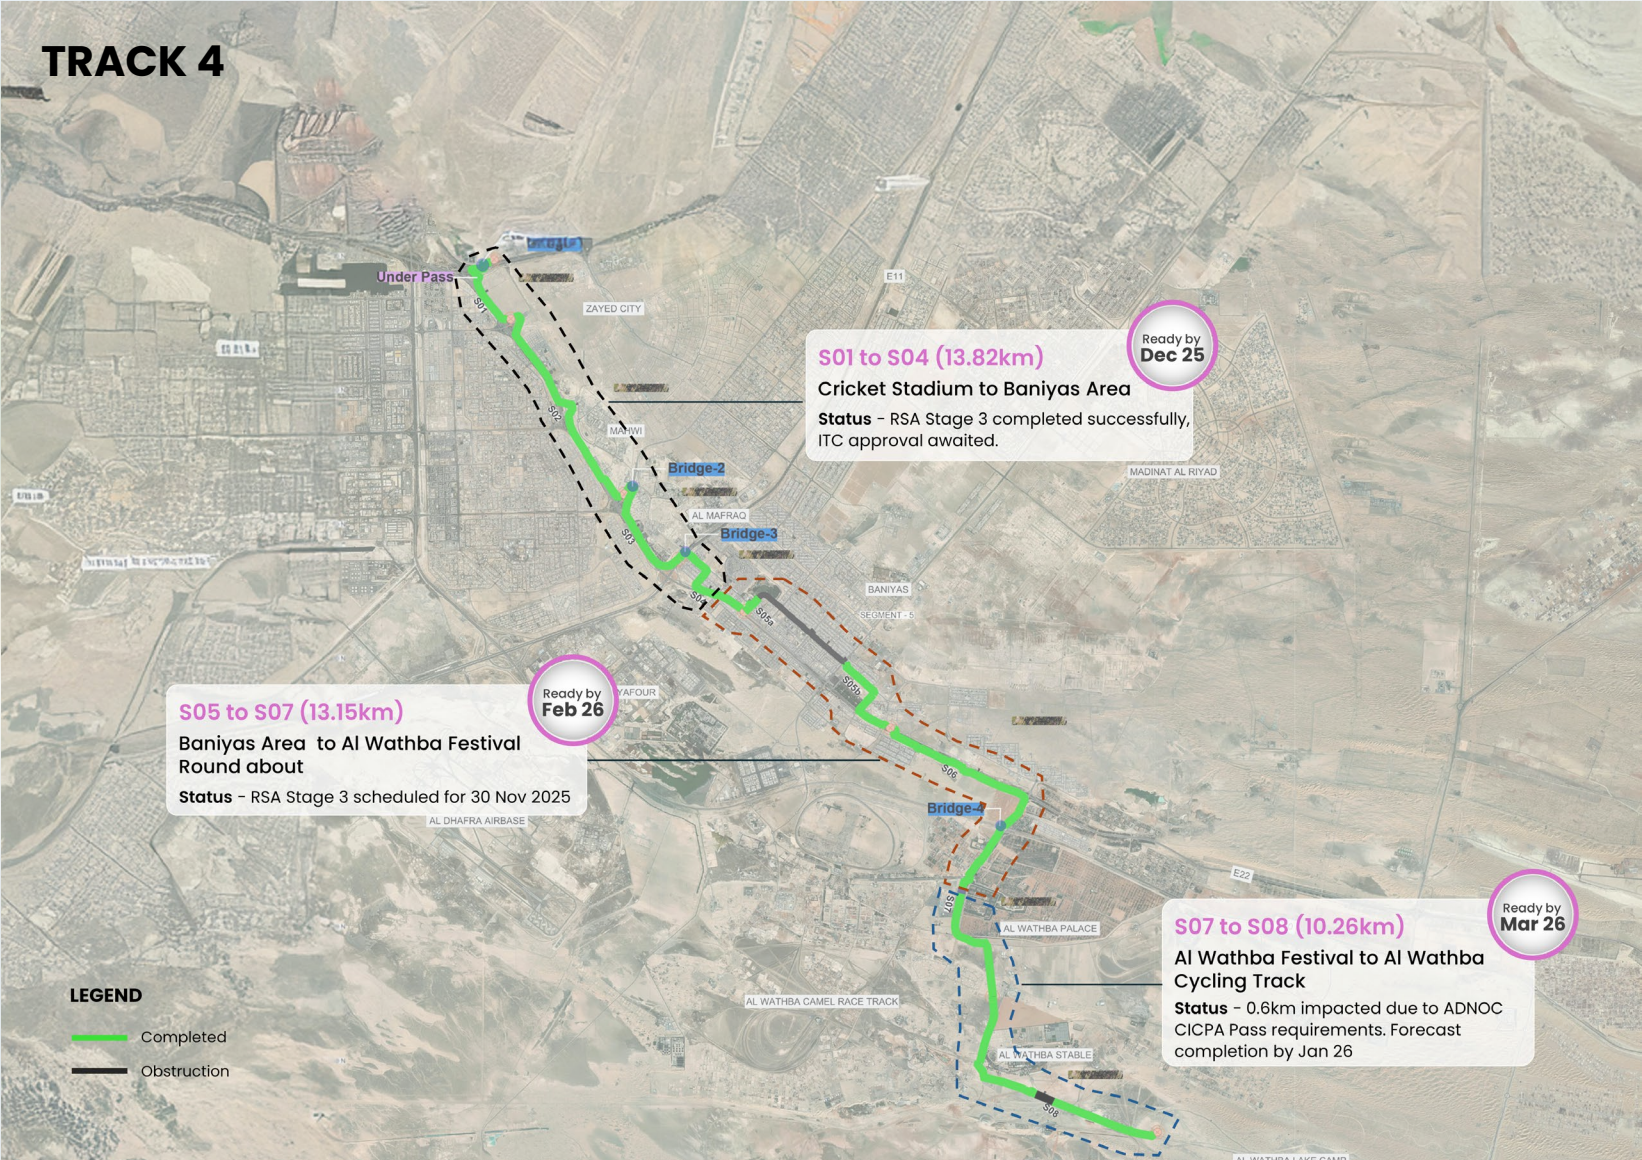

TRACK 03 & 04



Design Status

Completed



Contractor Procurement

Completed D&B



Construction

Ongoing

APR 2026

Forecast Completion



Description

Design & Build Project for Cycle track networks:

Route 3: Abu Dhabi Mainland to Abu Dhabi Boundary (Al Qudra)

Route 4: Abu Dhabi Mainland to South of Baniyas (Al Wathba)

Track 04

Cycle track	42.24 km (41.75 km asphalt completed)
Bridges	4 bridge (100%)
Underpass	1 underpass (100%)

Track 03

Cycle track	78.67 km (70.26 km asphalt completed)
Bridges	1 bridge (100%)
Nodes	2 Nodes (in Progress)




Route 4- Underpass



Cycle Track on Bridge deck



Bottom View Cycling deck

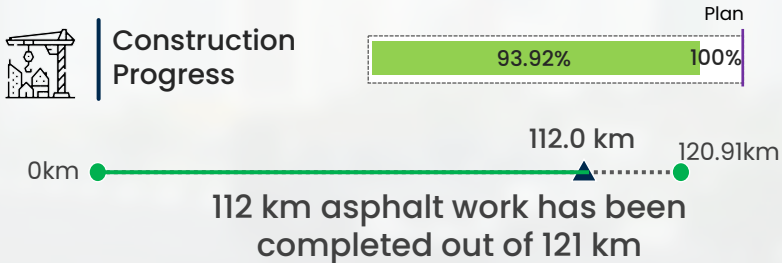

ABU DHABI CYCLE TRACK PROJECT

TRACK 02 – Section A


Design Status
PD Completed


Contractor Procurement
Completed D&B


Detailed Design
Started


Construction
Started



MAR 2027
Forecast
Completion



Description


Design & Build Project for Cycle track networks; Route 2-Section 1, connecting Yas Island to Sheikh Khalifa University and Mussafah Bridge.

Cycle track	37 km
Bridges	6 bridges
Underpasses	1 Underpass
Culverts	3 Culverts + 3 Utility Bridges

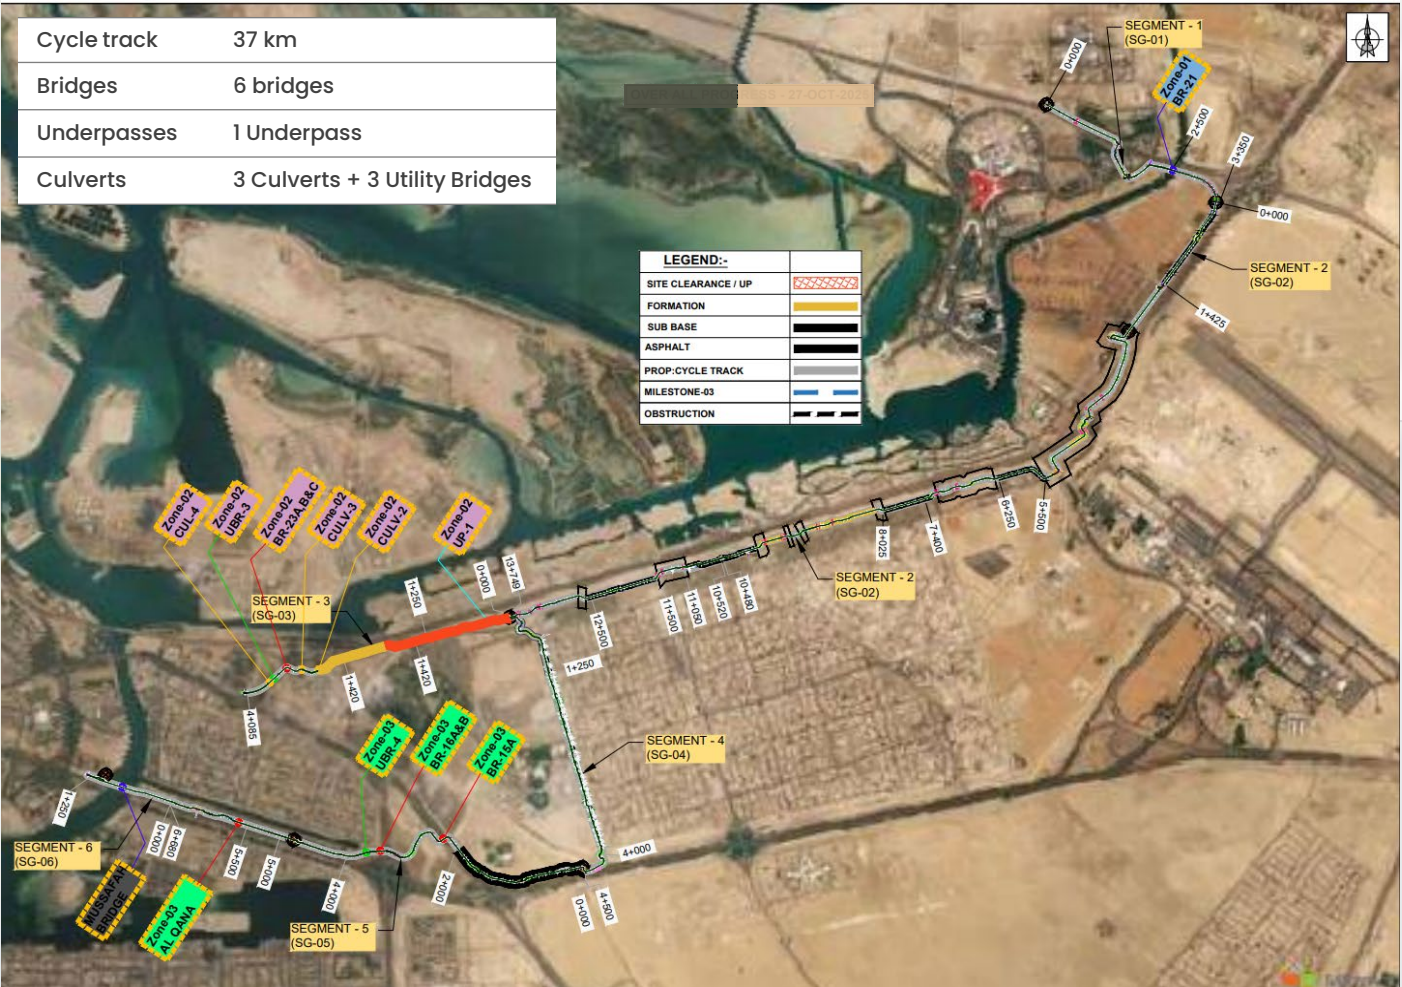

10 km asphalt work has been completed out of 37 km

Project Layout

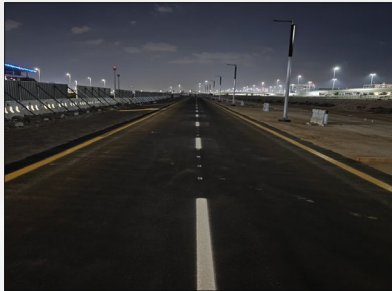



Design Status

CD Completed



Contractor Procurement

Completed D&B



Detailed Design

Not Started



Construction

Not Started

MAR 2028

Forecast Completion




Description

Design & Build Project for Cycle track networks; Route 2–Section B, Connecting Abu Dhabi Island to Saadiyat, Jubail, Fahid, and Yas Island

D&B kick off 21 Oct 2025. Designer Development (by Zutari) and Construction (by WBG)

Due to budget limitations and final decision on Sh Khalifa bridge connection, the procurement of the Route 2 Section B scope is a split of basic and optional scopes.

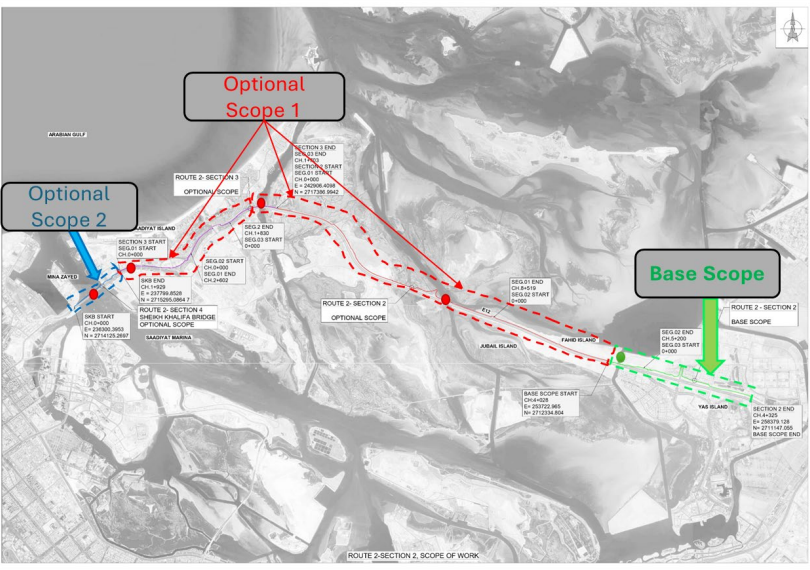

Base Scope : 5.5 km + 1 bridge
[From Yas Island to Fahid Island]

Optional Scope 1 : 21.0 KM + 3 bridges
[Fahid Island to Al Jubail and Saadiyat]

Optional Scope 2: Sheikh Khalifa Bridge,
Connecting Saadiyat Island to Abu Dhabi Island



Project Progress




Plan 1.28%




Actual 1.42%

Structures

Structure No.	Type of Crossing	Length (m)	No of Spans
BASE SCOPE			
BRIDGE-02/02	Water	295	7
OPTIONAL SCOPE 1			
BRIDGE-02/01	Water	75	2
BRIDGE-03/02	Water	852	21
BRIDGE-03/01	Road	31	1
OPTIONAL SCOPE 2			
Sheikh Khalifa Bridge Standalone bridge	Water	1,620	23
Track along the median of SKB	At-grade	3,500 (including ramps and road crossing bridges)	N/A



MAR 2028
Forecast
Completion

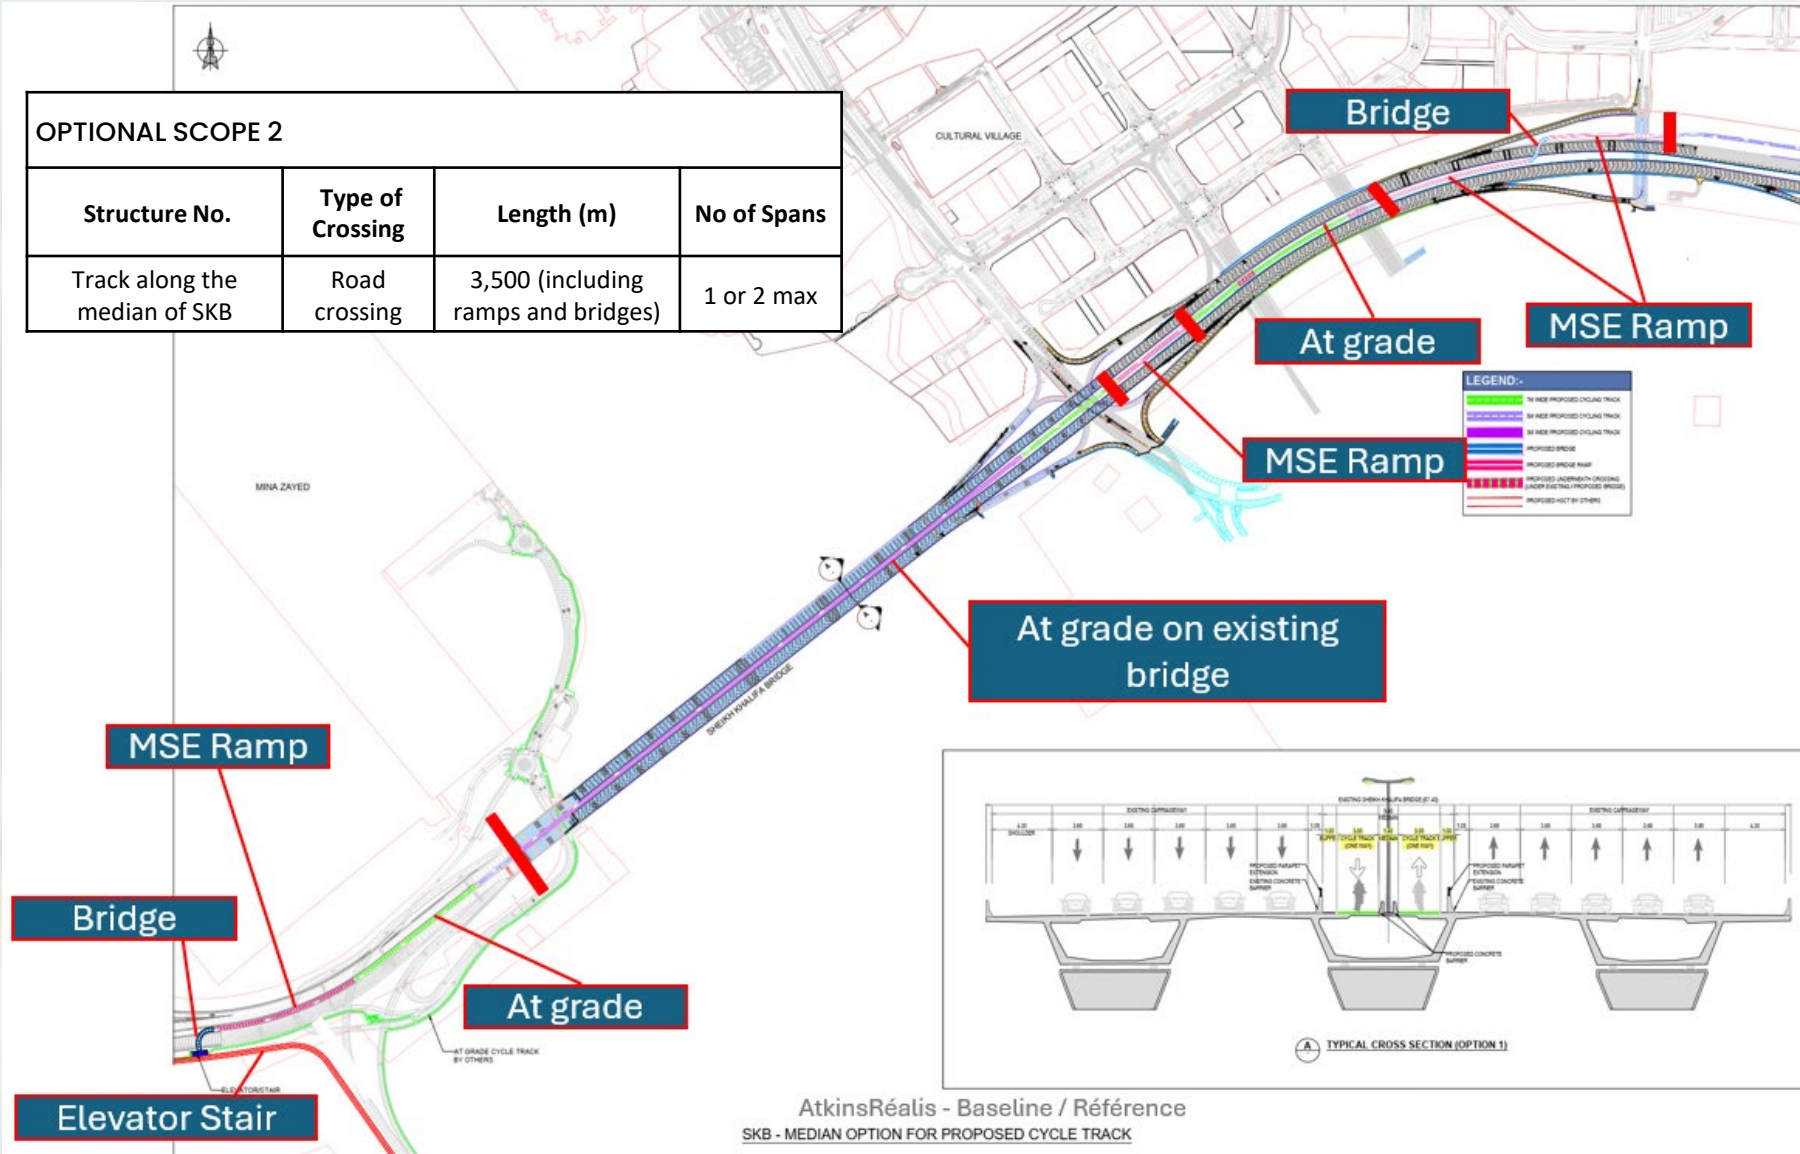



د. م. ت. م. ت.
DEPARTMENT OF MUNICIPALITIES
AND TRANSPORT

DMT/FP/COV/1/2025/12679
3 December 2025]

Mr. Adnan Abdulhadi Al Bnehi
Chief Executive Officer
Aidar Projects LLC

Subject: Confirmation on alignment profile viability assessment

The Department of Municipalities & Transport (DMT) extends its warmest greetings to you. We refer to your letter no. (ACT-FPOA-ALD-DMT-CTR-0014) dated 19 September 2025 regarding the above subject.

After reviewing the outcome of the submitted assessment, DMT confirms approval of providing the cycle track at the bed of the existing bridge.

Accordingly, please proceed with the next stage of the project, subject to the following conditions:

- Obtaining all necessary approvals (NOCs) from utility providers and relevant agencies, including ITC, DCT and ADM-TPO.
- Ensure the track design maintains a minimum width of 7.0 m wherever possible, in line with the ITC and DCT Guiding Network Basics of Design document.
- Please consider all safety and wind mitigation measures in your design for the safety of cyclists.

Please do not hesitate to contact Eng. Mohamed Al Qubaisi (Infrastructure Planning) at EDO.PP@dmnt.gov.ae should you have any queries regarding this matter

Best regards,



Abdulhadi Mohamed Ahmed Alilboushi
Acting Director General – Urban Planning & Permit Centre
Urban Planning & Permits Centre

The Client (M/S DMT) letter DMT/IFP/OUT/2025/12679 dated 3 December 2025 with informed decision to consider utilizing existing central median of SKB for the Cycle Track.

Aldar is engaging with ITC and concerned Authorities to obtain Approvals and NOCs.

HSCT– AD High-Speed Cycle Track


Design Status
CD Completed


Contractor Procurement
Completed D&B


Detailed Design
Not Started


Construction
Not Started

APR 2029
Forecast
Completion




Description

Design-Bid-Build closed loop,
A closed circuit strictly dedicated for sports users, with the following parameters:

- Total length is 52 KMs (closed Loop, one way)
- Width is 7m clear cycling track/ 8 meters full deck width
- Bridge type is a steel deck on steel piers
- #14 Access Ramps
- #2 Access staircase lifts

Design Status:

- Currently the loop is at the Schematic Design with 90% stage completion
- Planned completion of Design & Approvals is June 2026
- No Construction Budget is yet allocated

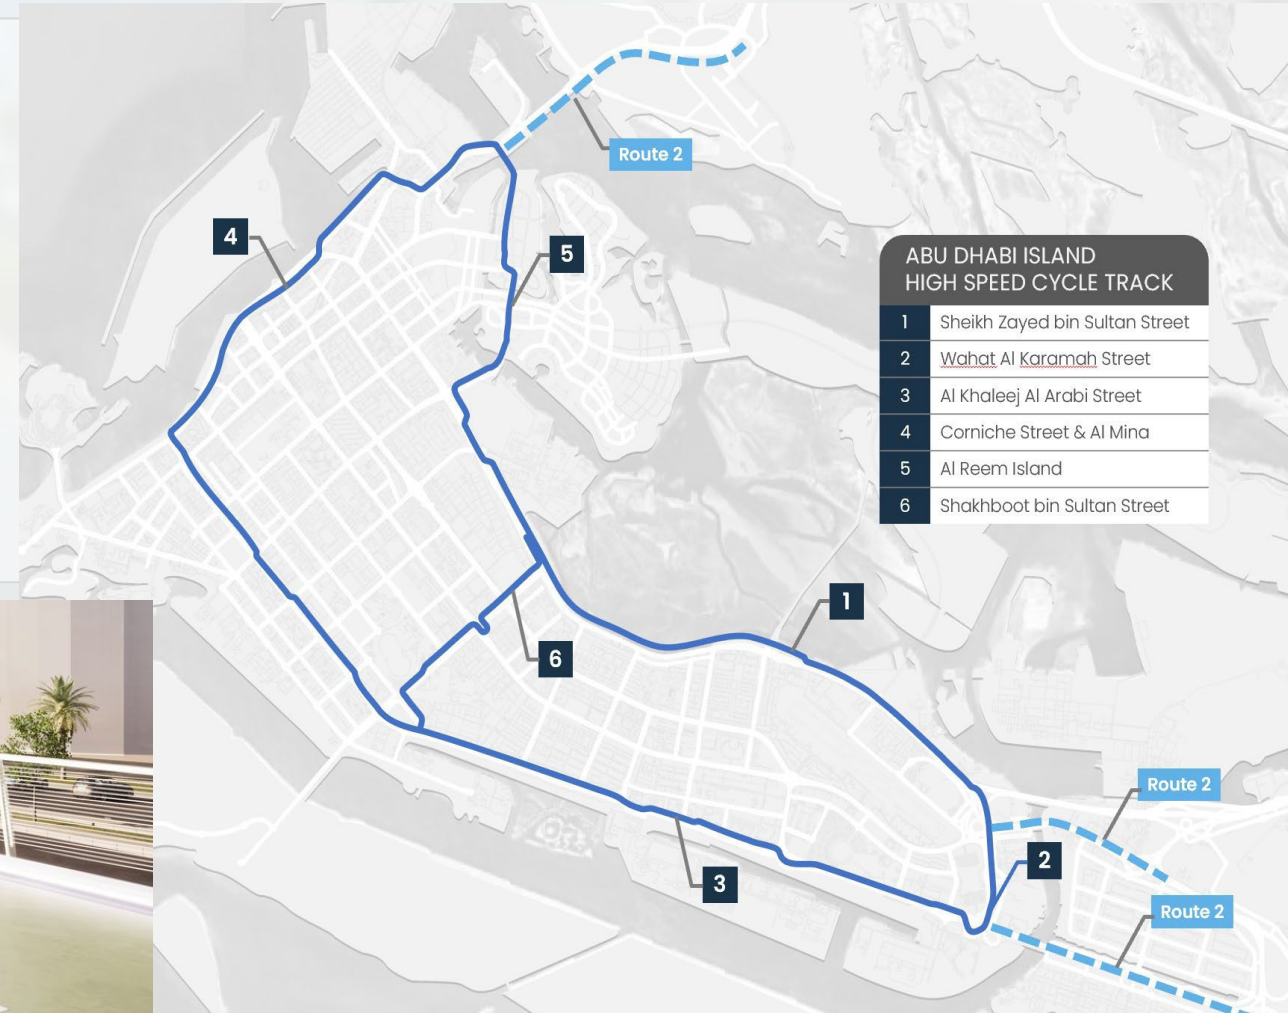



THANK YOU

ALDAR.COM
